Marine Operations Center - Pacific (SFO #09WSA0200C)

ID	Task Name	Start	Finish
58	**Final Design**	**Fri 11/13/09**	**Thu 4/29/10**
59	Design Document Preparation	Fri 11/13/09	Thu 4/29/10
60	Value Engineering with GC	Thu 12/10/09	Wed 1/20/10
61	Submit Design Documents for Review	Wed 1/20/10	Wed 1/20/10
62	Government Review	Thu 1/21/10	Wed 2/17/10
63	Receive Government Comments, Finalize Design Set	Thu 2/18/10	Wed 3/3/10
64	Submit Final Pier Design Documents	Thu 3/4/10	Thu 3/4/10
65	**Permitting**	**Mon 8/17/09**	**Tue 12/21/10**
66	**Sediment/Geotechnical Sampling in Bay**	**Mon 8/17/09**	**Fri 3/12/10**
67	Prepare Application	Mon 8/17/09	Fri 8/21/09
68	Submit Application	Mon 8/24/09	Mon 8/24/09
69	Permit Review & Issuance	Tue 8/25/09	Fri 9/18/09
70	**Building Permit (Pier)**	**Wed 1/20/10**	**Fri 3/12/10**
71	Submit Final Design Documents	Wed 1/20/10	Wed 1/20/10
72	Agency Review & Comment	Thu 1/21/10	Thu 2/18/10
73	Drawing Set Revision & Final Submission	Fri 2/19/10	Thu 3/4/10
74	Pier Building Permit Issued	Fri 3/12/10	Fri 3/12/10
75	**Building Permit (Buildings)**	**Mon 3/15/10**	**Fri 4/16/10**
76	Submit Application & CD Documents	Mon 3/15/10	Mon 3/15/10
77	Agency Review & Comment	Mon 3/15/10	Fri 4/2/10
78	CD Document Revision & Final Submission	Mon 4/5/10	Fri 4/9/10
79	Site Building Permit Issued	Fri 4/16/10	Fri 4/16/10
80	**Building Permit (Tenant Improvements)**	**Tue 6/29/10**	**Mon 8/2/10**
81	Submit Application & TI Design Set	Tue 6/29/10	Tue 6/29/10
82	Agency Review & Comment	Tue 6/29/10	Mon 7/19/10
83	CD Document Revision & Final Submission	Tue 7/20/10	Mon 7/26/10
84	Tenant Improvements Building Permit Issued	Mon 8/2/10	Mon 8/2/10
85	**JPA Fill/Removal Permit (USACE & DSL)**	**Mon 8/17/09**	**Thu 9/9/10**
86	Begin Agency Coordination for JPA	Mon 8/17/09	Mon 8/17/09
87	**Prepare JPA**	**Thu 9/17/09**	**Thu 12/10/09**
88	Application Form	Thu 9/17/09	Wed 12/9/09
89	Alternatives Analysis	Thu 9/17/09	Wed 12/9/09
90	Sampling and Analysis Plan (Sediment)	Thu 9/17/09	Wed 11/25/09
91	Biological Assessment	Thu 9/17/09	Wed 11/25/09
92	Meet with Agencies	Thu 12/10/09	Thu 12/10/09
93	Submit JPA	Thu 1/7/10	Thu 1/7/10
94	**Agency Reviews**	**Fri 1/8/10**	**Thu 9/9/10**
95	Completeness Review	Fri 1/8/10	Thu 1/28/10
96	**USACE**	**Fri 1/29/10**	**Thu 9/9/10**
97	30 Day Public Review	Fri 1/29/10	Thu 2/25/10
98	EIS / NEPA Write-up (as necessary)	Fri 1/29/10	Thu 3/25/10
99	**USACE Coordination**	**Fri 1/29/10**	**Thu 9/9/10**
100	Department of Land Conservation and Development - Coastal Mgmt. Prog.	Fri 1/29/10	Thu 2/25/10
101	Oregon DEQ - Water Quality 401 Certification	Fri 1/29/10	Thu 9/9/10
102	EPA - Section 404(b)(1) Clean Water Act	Fri 1/29/10	Thu 4/22/10
103	**NOAA / NMFS**	**Fri 1/29/10**	**Thu 6/17/10**
104	Biological Opinion (as necessary)	Fri 1/29/10	Thu 6/17/10
105	Essential Fish Habitat Assessment	Fri 1/29/10	Thu 6/17/10
106	Regional Sediment Evaluation Team - Sediment Evaluation Framework	Fri 1/29/10	Thu 4/22/10
107	**DSL**	**Fri 1/29/10**	**Thu 5/20/10**
108	DSL Review	Fri 1/29/10	Thu 5/20/10
109	ODFW Review/Coordination	Fri 1/29/10	Thu 2/25/10
110	**Permit(s)/Approval(s) Issued**	**Fri 4/23/10**	**Mon 9/13/10**
111	DEQ Water Quality 401 Certification Approval	Fri 9/10/10	Fri 9/10/10
112	EPA 404(b)(1) Approval	Fri 4/23/10	Fri 4/23/10
113	RSET Approval	Fri 4/23/10	Fri 4/23/10
114	DSL Fill/Removal Permit Issued	Thu 6/3/10	Thu 6/3/10

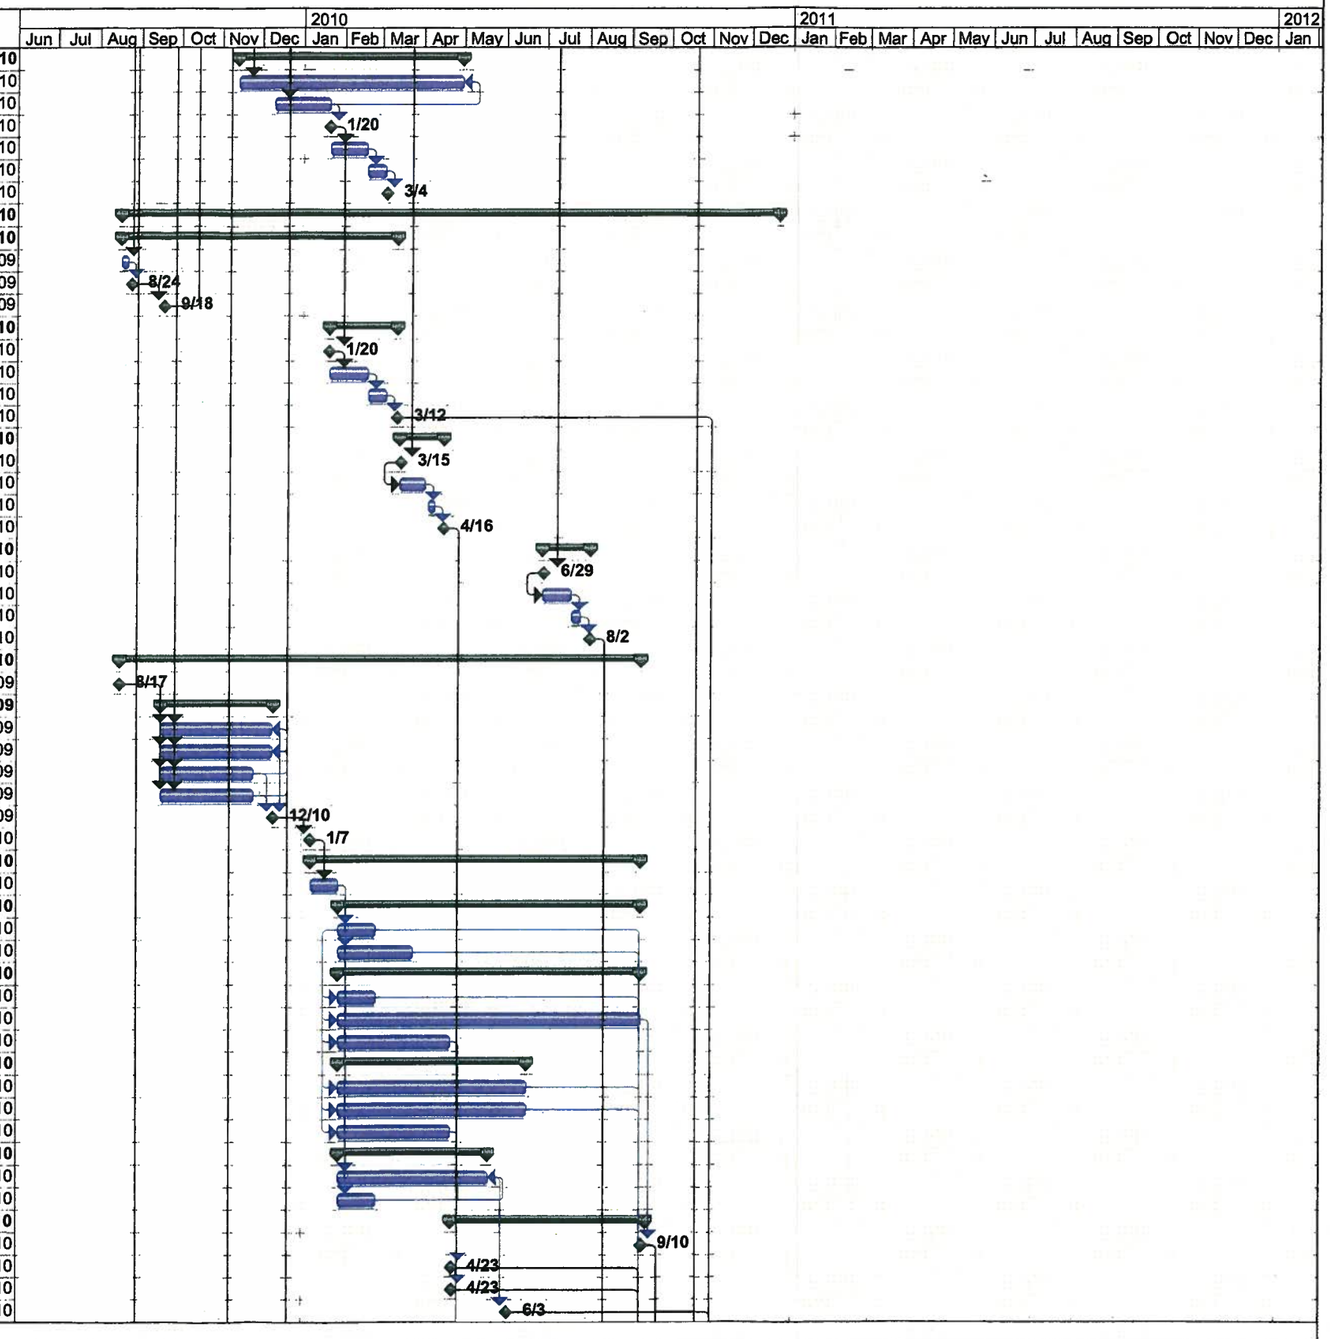

Project: MOC-P
Date: Sat 5/30/09

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
