Marine Operations Center - Pacific (SFO #09WSA0200C)

ID	Task Name	Start	Finish
1	Project Award	Mon 8/3/09	Mon 8/3/09
2	Receive Notice to Proceed (NTP)	Fri 8/14/09	Fri 8/14/09
3	Award Contract(s) to Design Team	Fri 8/14/09	Fri 8/14/09
4	**Design Charette**	**Mon 8/17/09**	**Tue 8/18/09**
5	Site Design Charrette	Mon 8/17/09	Mon 8/17/09
6	Eco-Design Charrette	Tue 8/18/09	Tue 8/18/09
7	Hire Project Manager	Wed 9/16/09	Wed 9/16/09
8	**Construction Manager/General Contractor (CMGC) Proposal & Selection Process**	**Thu 9/17/09**	**Wed 12/9/09**
9	Advertise Solicitation for CMGC	Thu 9/17/09	Wed 10/14/09
10	NTP Awarded to CMGC	Wed 12/9/09	Wed 12/9/09
11	**Design Documents**	**Tue 8/18/09**	**Mon 6/28/10**
12	**Site Design**	**Tue 8/18/09**	**Mon 6/28/10**
13	Field Investigation & Survey	Tue 9/1/09	Fri 10/2/09
14	Geotech Report Complete	Fri 10/30/09	Fri 10/30/09
15	**Preliminary/Schematic Design (SD)**	**Tue 8/18/09**	**Wed 9/16/09**
16	SD Preparation	Tue 8/18/09	Tue 9/15/09
17	Submit SD Set	Wed 9/16/09	Wed 9/16/09
18	**Design Development (DD) & Spec Outline**	**Wed 9/16/09**	**Fri 12/11/09**
19	DD Drawings & Spec Outline Preparation	Wed 9/16/09	Thu 12/10/09
20	Submit Working DD Set for Review	Tue 10/27/09	Tue 10/27/09
21	Government Review	Wed 10/28/09	Tue 11/24/09
22	Incorporate Government Comments & Finalize DD Set	Wed 11/25/09	Thu 12/10/09
23	Submit Final DD Documents	Fri 12/11/09	Fri 12/11/09
24	**Construction Documents (CDs) & Specs**	**Thu 12/10/09**	**Mon 6/28/10**
25	**Site Prep & Building Structure**	**Thu 12/10/09**	**Fri 3/12/10**
26	Design Document Preparation	Mon 12/14/09	Mon 2/15/10
27	Value Engineering with GC	Thu 12/10/09	Wed 1/20/10
28	Submit Working CD Set for Review	Fri 1/15/10	Fri 1/15/10
29	Government Review	Mon 1/18/10	Fri 2/12/10
30	Receive Government Comments	Mon 2/15/10	Mon 2/15/10
31	Finalize CD Documents	Mon 2/15/10	Thu 3/11/10
32	Submit Final CD Documents	Fri 3/12/10	Fri 3/12/10
33	**Building Shell & Site Work**	**Thu 12/10/09**	**Fri 3/12/10**
34	Design Document Preparation	Mon 12/14/09	Mon 2/15/10
35	Value Engineering with GC	Thu 12/10/09	Wed 1/20/10
36	Submit Working CD Set for Review	Fri 1/15/10	Fri 1/15/10
37	Government Review	Mon 1/18/10	Fri 2/12/10
38	Receive Government Comments	Mon 2/15/10	Mon 2/15/10
39	Finalize CD Documents	Mon 2/15/10	Thu 3/11/10
40	Submit Final CD Documents	Fri 3/12/10	Fri 3/12/10
41	**Tenant Improvements (TI)**	**Mon 1/18/10**	**Mon 6/28/10**
42	Design Document Preparation	Mon 1/18/10	Fri 5/21/10
43	Value Engineering with GC	Mon 3/8/10	Fri 4/16/10
44	Submit Design Documents for Review	Mon 4/19/10	Mon 4/19/10
45	Government Review	Tue 4/20/10	Fri 5/21/10
46	Receive Government Comments	Fri 5/21/10	Fri 5/21/10
47	Finalize TI Design Documents	Mon 5/24/10	Fri 6/25/10
48	Submit Final TI Design Set	Mon 6/28/10	Mon 6/28/10
49	**Pier Design**	**Tue 8/18/09**	**Thu 4/29/10**
50	**20% Design**	**Tue 8/18/09**	**Wed 9/16/09**
51	Design Document Preparation	Tue 8/18/09	Tue 9/15/09
52	Submit Design Documents	Wed 9/16/09	Wed 9/16/09
53	**30% Design**	**Wed 9/16/09**	**Thu 11/12/09**
54	Design Document Preparation	Wed 9/16/09	Thu 10/15/09
55	Submit Design Documents for Review	Thu 10/15/09	Thu 10/15/09
56	Government Review	Fri 10/16/09	Thu 11/12/09
57	Receive Government Comments	Thu 11/12/09	Thu 11/12/09

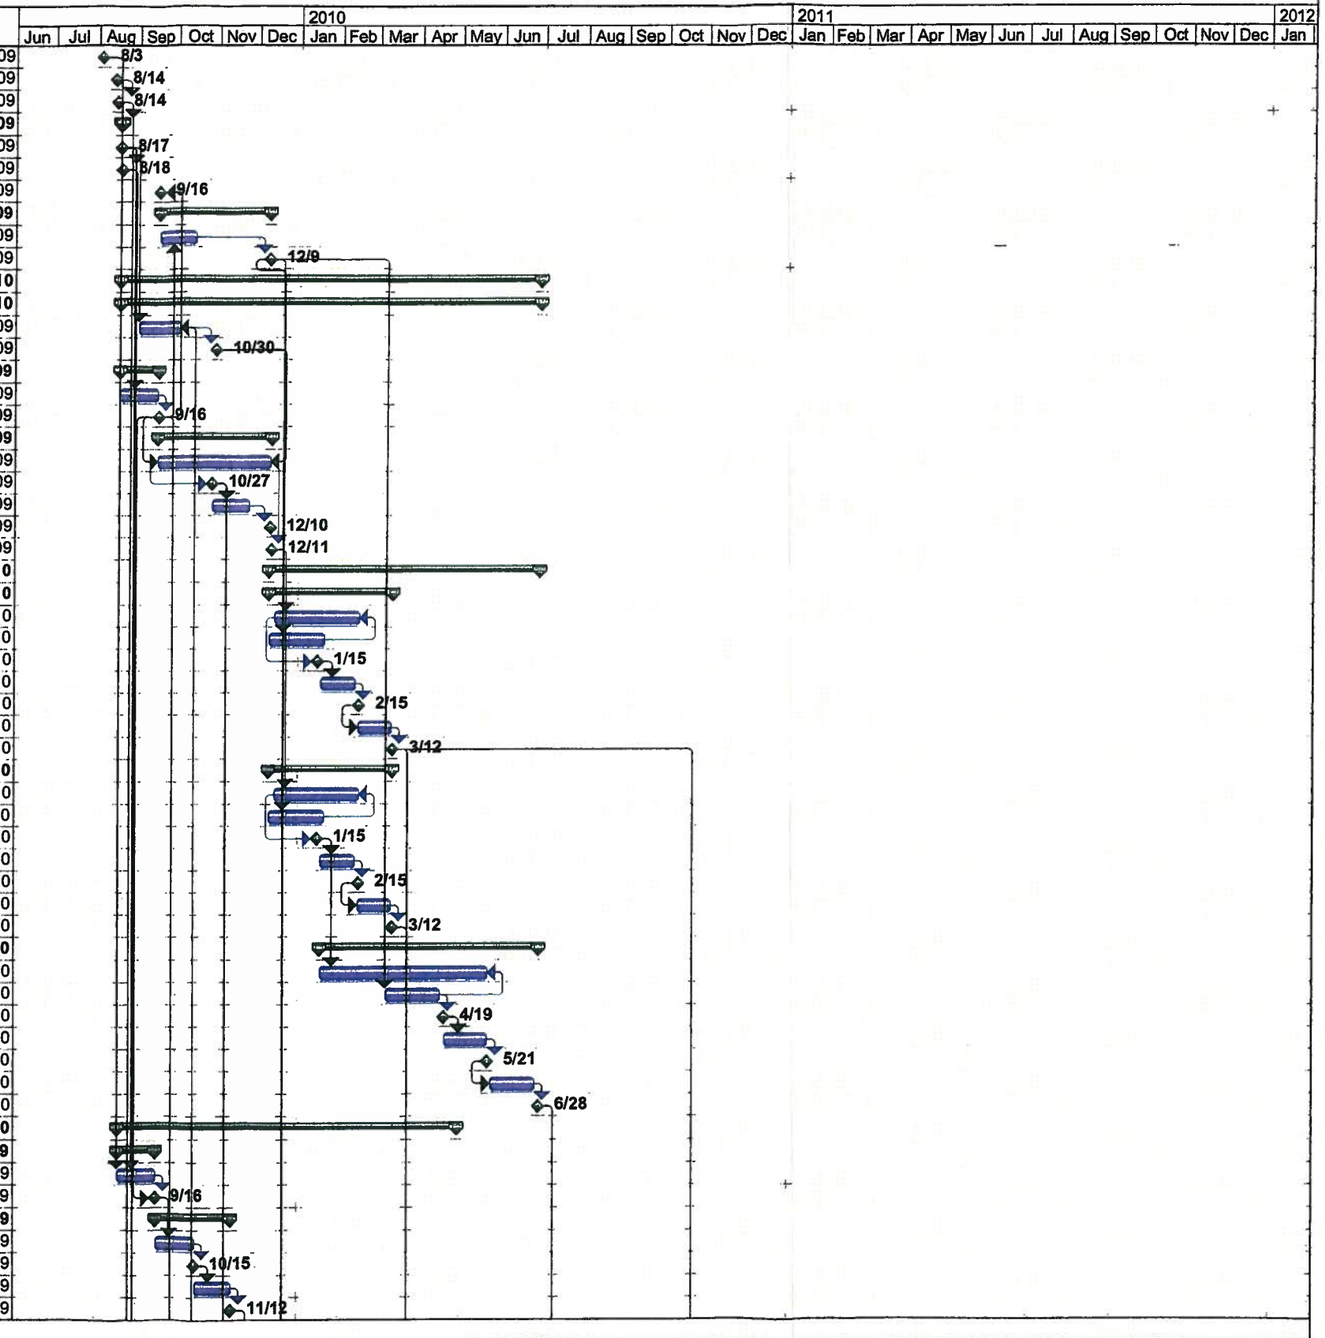

Project: MOC-P
Date: Sat 5/30/09

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
