Marine Operations Center - Pacific (SFO #09WSA0200C)

ID	Task Name	Start	Finish
115	USACE Section 10/Section 404 Permit(s) Issued	Mon 9/13/10	Mon 9/13/10
116	**DEQ Erosion & Sediment Control (ESC)**	**Wed 10/28/09**	**Thu 11/26/09**
117	Submit 1200-C Application and Erosion & Sediment Control Drawings	Wed 10/28/09	Wed 10/28/09
118	1200-C Permit Issued	Thu 11/26/09	Thu 11/26/09
119	**DEQ Permit to Discharge Storm Runoff to the Bay (1200-Z)**	**Mon 10/25/10**	**Tue 12/21/10**
120	Submit 1200-Z Application & Drawings	Mon 10/25/10	Mon 10/25/10
121	1200-Z Permit Issued	Tue 12/21/10	Tue 12/21/10
122	**Construction**	**Thu 12/3/09**	**Fri 7/1/11**
123	**Site**	**Thu 12/3/09**	**Sun 5/1/11**
124	Mobilization	Thu 12/3/09	Wed 12/9/09
125	Placement of ESC Materials	Thu 12/10/09	Wed 12/16/09
126	Demolition of Existing Land Structures & Rough Grading	Thu 12/17/09	Tue 3/9/10
127	Site Prep & Building Structure	Mon 4/19/10	Fri 9/3/10
128	Substantial Completion	Thu 8/5/10	Thu 8/5/10
129	Tenant Improvements	Tue 8/3/10	Mon 1/17/11
130	Construction Complete	Tue 1/18/11	Tue 1/18/11
131	Commissioning	Wed 1/19/11	Tue 2/15/11
132	Building Occupancy	Sun 5/1/11	Sun 5/1/11
133	**Pier**	**Mon 11/1/10**	**Fri 7/1/11**
134	**In-Water Work Period**	**Mon 11/1/10**	**Tue 2/15/11**
135	In-water period	Mon 11/1/10	Tue 2/15/11
136	Demolish Existing Structures (In-water work)	Mon 11/1/10	Fri 12/10/10
137	Dredging	Mon 11/1/10	Fri 12/24/10
138	Install New Pier Piles	Mon 11/1/10	Tue 2/15/11
139	Pier Surface (Non-water Work)	Wed 12/22/10	Tue 4/26/11
140	Substantial Completion	Fri 4/15/11	Fri 4/15/11
141	4 Berths Complete	Fri 4/29/11	Fri 4/29/11
142	Complete Remaining 2 Berths	Mon 5/2/11	Fri 7/1/11
143	Last 2 Berths Complete	Fri 7/1/11	Fri 7/1/11
144	**LEED Certification**	**Wed 8/19/09**	**Mon 1/2/12**
145	Development of Points and Initial Paperwork	Wed 8/19/09	Fri 4/1/11
146	Certification Commissioning & Documentation Process	Mon 4/4/11	Fri 12/30/11
147	LEED Silver Certification Issued	Mon 1/2/12	Mon 1/2/12

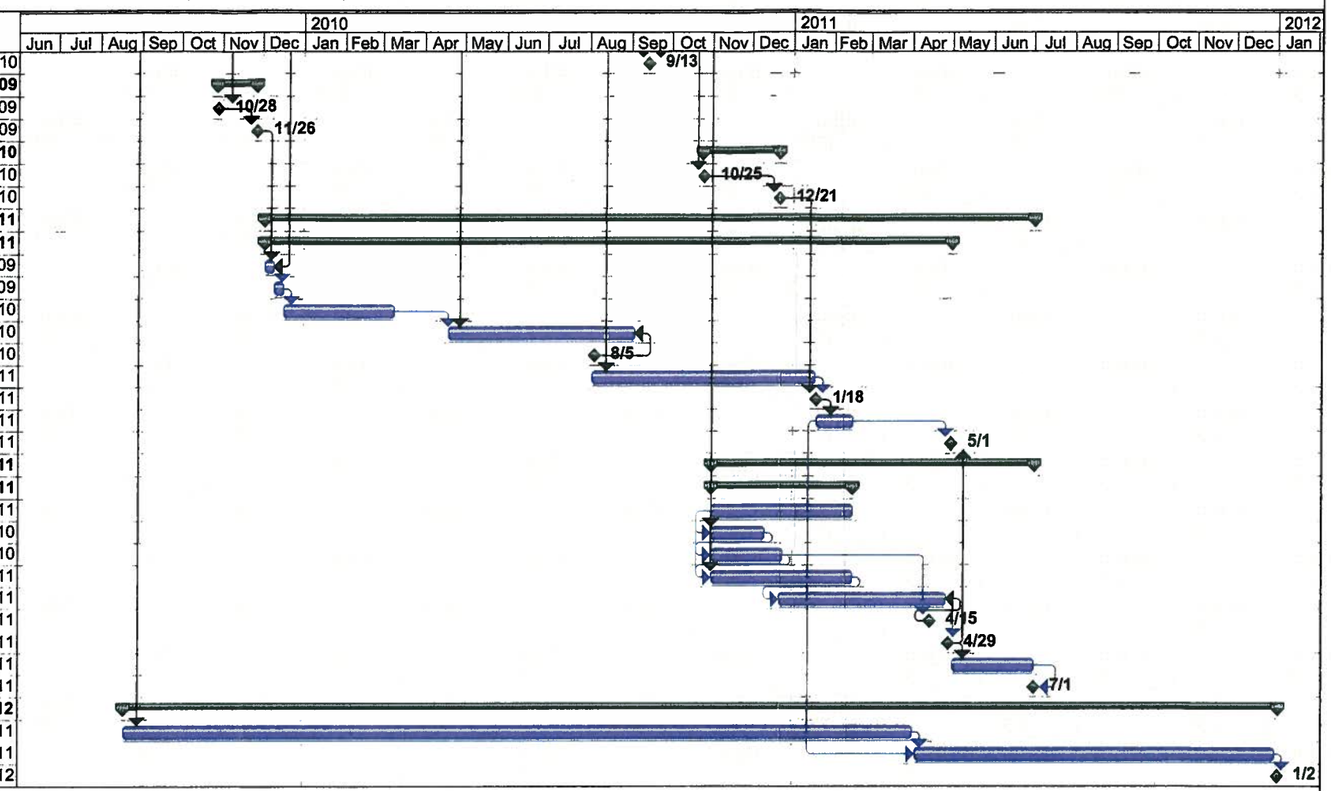

Project: MOC-P
Date: Sat 5/30/09

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
